



2025 TOWN OF FORKS PROGRESS SCHEDULE

P.O. Box 1058
Ridgefield, WA 98642

PROJECT NAME

2025 CITY WIDE CHIP SEAL PROJECT

START DATE

8/4/2025

CONTRACTOR

SIERRA SANTA FE CORPORATION

END DATE

TBD

TIMELINE																		
PHASE TITLE	START DATE	END DATE	DURATION (IN DAYS)	8/4	8/5	8/6	8/7	8/8	8/11	8/12	8/13	8/14	8/15	8/18	8/19	8/20	8/21	8/22
Pulverization	8/4/25	8/8/25	5															
Pulverization	8/11/25	8/15/25	5															
Pulverization	8/18/25	8/22/25	5															


TIMELINE														
PHASE TITLE	START DATE	END DATE	DURATION (IN DAYS)	8/25	8/26	8/27	8/28	8/29	9/1	9/2	9/3	9/4	9/5	
Chip Seal	8/25/25	8/29/25	5											
Sweeping	8/25/25	8/29/25	5											
Sweeping	9/2/25	9/3/25	2											
Fog Seal	9/2/25	9/3/25	2											
Pavement Markings	TBD	TBD	TBD											

2025 City of Forks

Red: Single Chip
Yellow: Pulv & Double Chip

Day 1 8/27: 1-30
Day 2 8/28: 31-55 & 6-15
Day 3 8/29: 2-4 & 56-84
Day 4 9/2: 2nd layer of yellow 19-84

Legend

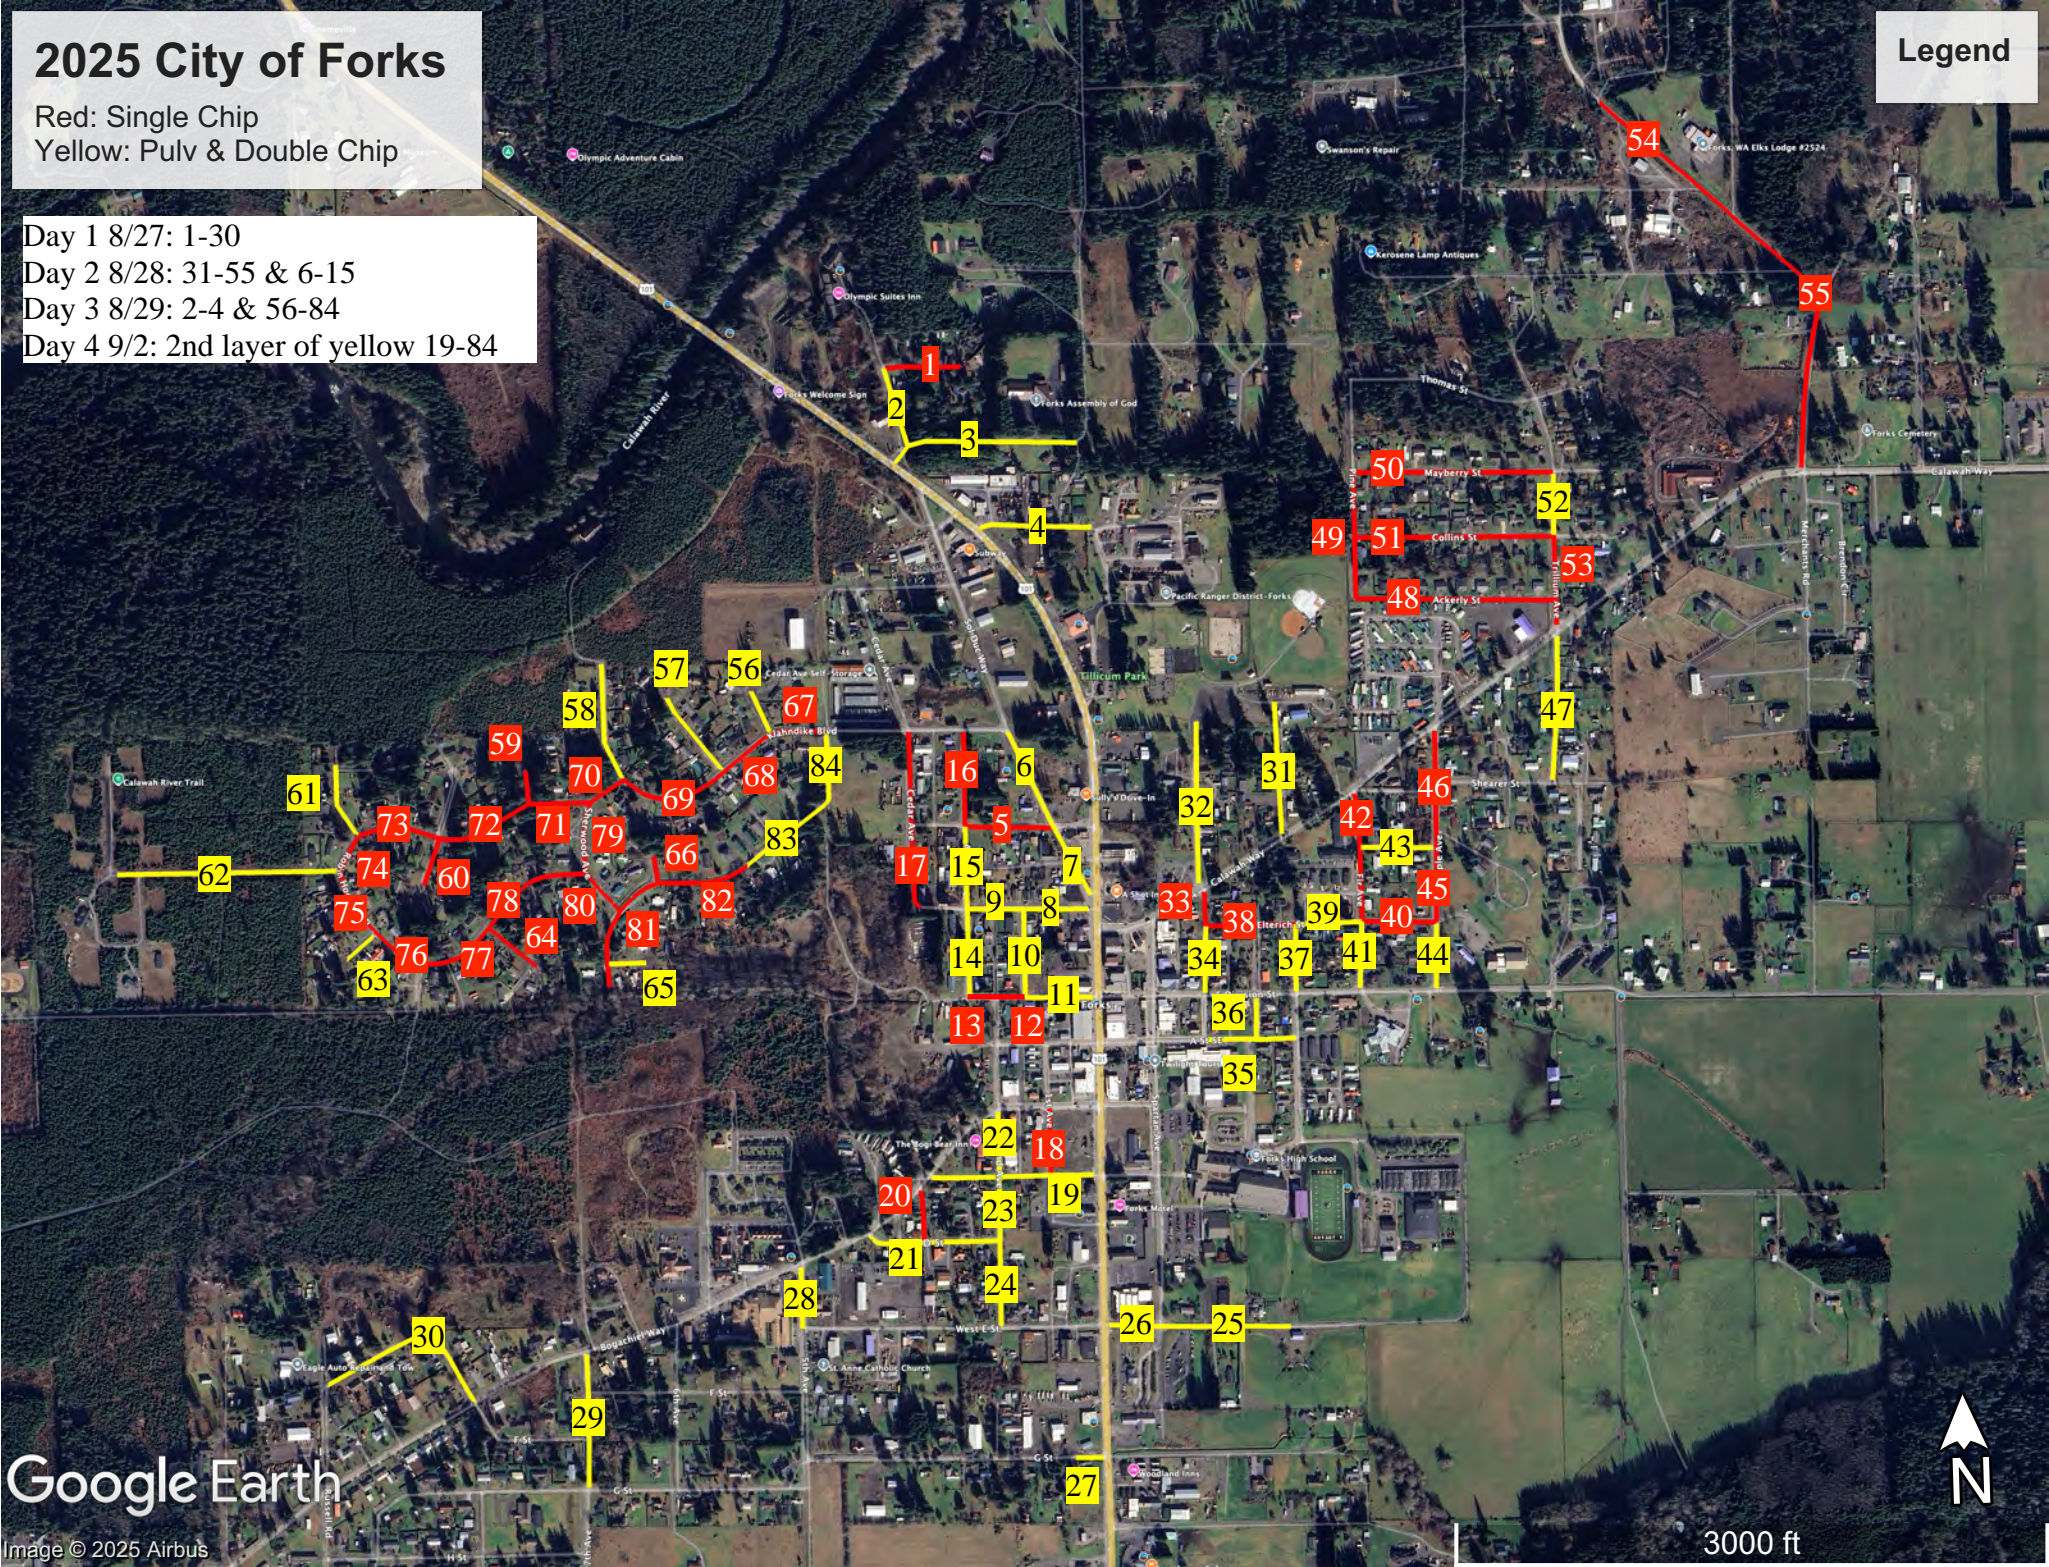

Google Earth

Image © 2025 Airbus

3000 ft
